

- ¹⁴ Attach Certificate from Chartered Accountant
¹⁵ Attach Certificates from Engineers –in- Charge

Letter of Acceptance

(letterhead paper of the Employer)

_____ [date]

To: _____ [name and address of
the Contractor]

Dear Sirs,

This is to notify you that your Tender dated _____ for execution of the _____ [name
of the contract and identification number, as given in the Instructions to Tenderers] for the Contract Price of Rupees
_____ (_____) [amount in words
and figures], as corrected and modified in accordance with the Instructions to Tenderers is hereby accepted by our
Agency.

You are hereby requested to furnish Security deposit, in the form detailed in Para 24.1 of ITT for an amount of
Rs. _____ within 20 days of the receipt of this letter of acceptance valid up to 30 days from the date of expiry
of Defects Liability Period i.e. up to and sign the contract, failing which action as stated in Para 24.3 of ITT
will be taken.

Yours faithfully,

Authorized Signature

Name and Title of Signatory

Name of Agency

Issue of Notice to proceed with the work

(letterhead of the Employer)

_____ (date)

To

_____ (name and address of the Contractor)


Dear Sirs:

Pursuant to your furnishing the requisite Security deposit as stipulated in ITT Clause 24.1 and signing of the contract
agreement for the construction of _____¹⁶ a Tender Price of Rs. _____, you are hereby instructed to
proceed with the execution of the said works in accordance with the contract documents.

Yours faithfully,

(Signature, name and title of signatory authorized to sign on behalf of Employer)

T. Jif


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

16 Give the name of the Contract

Agreement Form

Agreement

This agreement, made the _____ day of _____ 20_____,
between _____
[name and address of Employer]
(hereinafter called "the Employer") of the one part and _____
[name and address of contractor] (hereinafter called
"the Contractor") of the other part.


Whereas the Employer is desirous that the Contractor execute _____
[name and
identification number of Contract] (hereinafter called "the Works") and the Employer has accepted the Tender by
the Contractor for the execution and completion of such Works and the remedying of any defects therein at a
contract price of Rupees.....

NOW THIS AGREEMENT WITNESSETH as follows:

1. In this Agreement, words and expression shall have the same meanings as are respectively assigned to them in the Conditions of Contract hereinafter referred to, and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy any defects therein in conformity in all aspects with the provisions of the Contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying the defects wherein the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.
4. The following documents shall be deemed to form and be read and construed as part of this Agreement, viz:
 - i) Letter of Acceptance;
 - ii) Notice to proceed with the works;
 - iii) Contractor's Tender;
 - iv) Contract Data;
 - v) Conditions of contract (including Special Conditions of Contract);
 - vi) Specifications;
 - vii) Drawings;
 - viii) Bill of Quantities; and
 - ix) Any other document listed in the Contract Data as forming part of the contract.

In witness whereof the parties thereto have caused this Agreement to be executed the day and year first before written.

Page 18 of 34


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

The Common Seal of _____
was hereunto affixed in the presence of:
Signed, Sealed and Delivered by the said _____

in the presence of:
Binding Signature of Employer _____
Binding Signature of Contractor _____

SECTION 4: CONDITIONS OF CONTRACT

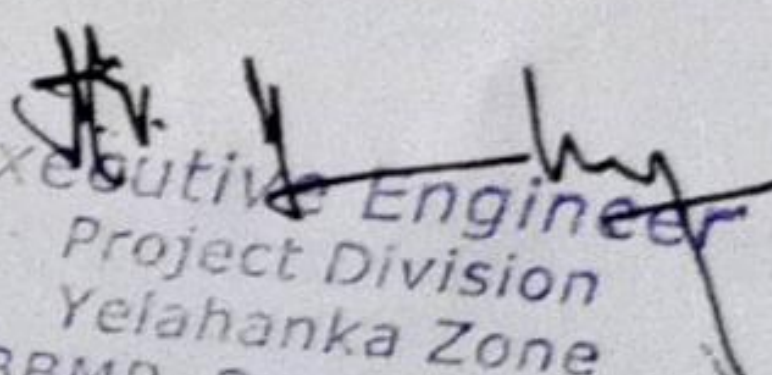
Table of Contents

A. General Page No.

1. Definitions 18
2. Interpretation 18
3. Law governing contract 19
4. Employers decisions 19
5. Delegation 19
6. Communications 19
7. Subcontracting 19
8. Other Contractors 19
9. Personnel 19
10. Employer's and Contractor's risks 19
11. Employer's risks 19
- 12 Contractor's risks 20
- 13 Query about Contract Data 20
- 14 Contractor to construct the Works 20
15. The Works to be completed by Intended Completion Date 20
16. Safety 20
17. Discoveries 20
18. Possession of the Site 20
19. Access to the Site 20
20. Instructions 20

B. Time Control

21. Program 20
22. Extension of the Intended Completion Date 21
23. Delays ordered by the Employer 21


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

24. Management meetings	21
C. Quality Control	
25. Identifying defects	21
26. Tests	21
27. Correction of defects	21
28. Uncorrected defects	21
D. Cost Control	
29. Bill of Quantities (BOQ)	21
30. Variations	22
31. Payment for Variations	22
32. Submission of bills for payment	22
33. Payments	23
34. Compensation events	23
35. Tax	23
36. Liquidated damages	23
37. Cost of repairs	24
E Finishing of Contract	
38. Completion	24
39. Taking Over	24
40. Final account	24
41. As built drawings	24
42. Termination	24
43. Payment upon termination	25
44. Property	25
45. Release from performance	25
F Special Conditions of Contract	

Conditions of Contract

A. General

1. Definitions

1.1 Terms which are defined in the Contract Data are not also defined in the Conditions of Contract but keep their defined meanings. Bold letters are used to identify defined terms.

Bill of Quantities means the priced and completed Bill of Quantities forming part of the Tender.

Compensation events are those defined in Clause 34 hereunder.

The **Completion Date** is the date of completion of the Works as certified by the Employer in accordance with Sub Clause 38.1.

The **Contract** is the contract between the Employer and the Contractor to execute, complete and maintain the Works. It consists of the documents listed in Clause 2.3 below.

The **Contract Data** defines the documents and other information which comprise the Contract.

The **Contractor** is a person or corporate body whose Tender to carry out the Works has been accepted by the Employer.

The **Contractor's Tender** is the completed Tender document submitted by the Contractor to the Employer.

The **Contract price** is the price stated in the Letter of Acceptance and thereafter as adjusted in accordance with the provisions of the Contract.

Days are calendar days; **months** are calendar months.

A **Defect** is any part of the Works not completed in accordance with the Contract.

The **Defects liability period** is the period named in the Contract Data and calculated from the Completion Date.

The **Employer** is the party who will employ the Contractor to carry out the Works.

Equipment is the Contractor's machinery and vehicles brought temporarily to the Site to construct the Works.

The **Initial Contract price** is the Contract Price listed in the Employer's Letter of Acceptance.

The **Intended Completion Date** is the date on which it is intended that the Contractor shall complete the Works. The Intended Completion Date is specified in the Contract Data. The Intended Completion Date may be revised only by the Employer by issuing an extension of time.

Materials are all supplies, including consumables, used by the contractor for incorporation in the Works.

Plant is any integral part of the Works which is to have a mechanical, electrical, electronic or chemical or biological function.

The **Site** is the area defined as such in the Contract Data.

Specification means the Specification of the Works included in the Contract and any modification or addition made or approved by the Employer.

The **Start Date** is given in the Contract Data. It is the date when the Contractor shall commence execution of the works. It does not necessarily coincide with any of the Site Possession Dates.

A **Subcontractor** is a person or corporate body who has a Contract with the Contractor to carry out a part of the work in the Contract which includes work on the Site.

A **Variation** is an instruction given by the Employer which varies the Works.

The Works are what the Contract requires the Contractor to construct, install, and turn over to the Employer, as defined in the Contract Data.

2. Interpretation

2.1 In interpreting these Conditions of Contract, singular also means plural, male also means female or neuter, and the other way around. Headings have no significance. Words have their normal meaning under the language of the Contract unless specifically defined. The Employer will provide instructions clarifying queries about the Conditions of Contract.

2.2 The documents forming the Contract shall be interpreted in the following order of priority:

- (1) Agreement
- (2) Letter of Acceptance, notice to proceed with the works
- (3) Contractor's Tender
- (4) Contract Data
- (5) Conditions of Contract
- (6) Specifications
- (7) Drawings
- (8) Bill of quantities and
- (9) any other document listed in the Contract Data as forming part of the Contract.

3. Law governing contract

3.1 The law governing the Contract is the Laws of India supplanted by the Karnataka Local Acts.

4. Employer's decisions

4.1 Except where otherwise specifically stated, the Employer will decide contractual matters between the Employer and the Contractor.

5. Delegation

5.1 The Employer may delegate any of his duties and responsibilities to other people after notifying the Contractor and may cancel any delegation after notifying the Contractor.

6. Communications

6.1 Communications between parties which are referred to in the conditions are effective only when in writing. A notice shall be effective only when it is delivered (in terms of Indian Contract Act).

7. Subcontracting

7.1 The Contractor may subcontract with the approval of the Employer but may not assign the Contract without the approval of the Employer in writing. Subcontracting does not alter the Contractor's obligations.

8. Other Contractors

8.1 The Contractor shall cooperate and share the Site with other contractors, public authorities, utilities, and the Employer.

9. Personnel

9.1 The Contractor shall employ the technical personnel (of number and qualifications) as may be stipulated by GOK from time to time during the execution of the work. The technical staff so employed shall be available at site as may be stipulated by the Employer.

9.2 If the Employer asks the Contractor to remove a person who is a member of the Contractor's staff or his work force stating the reasons, the Contractor shall ensure that the person leaves the Site within seven days and has no further connection with the work in the Contract.

10. Employer's and Contractor's risks

10.1 The Employer carries the risks which this Contract states are Employer's risks, and the Contractor carries the risks which this Contract states are Contractor's risks.

11. Employer's risks

11.1 The Employer is responsible for the excepted risks which are (a) in so far as rebellion, riot commotion or disorder or (b) a cause due solely to the design of the Works, other than the Contractor's design.

12. Contractor's risks

12.1 All risks of loss of or damage to physical property and of personal injury and death which arise during and in consequence of the performance of the Contract other than the excepted risks are the responsibility of the Contractor.

13. Queries about the Contract Data

13.1 The Employer will clarify queries on the Contract Data.

14. Contractor to construct the Works

14.1 The Contractor shall construct the Works in accordance with the Specification and Drawings.

15. The Works to be completed by the Intended Completion Date

15.1 The Contractor may commence execution of the Works on the Start Date and complete them by the Intended Completion Date.

16. Safety

16.1 The Contractor shall be responsible for the safety of all activities on the Site.

17. Discoveries

17.1 Anything of historical or other interest or of significant value unexpectedly discovered on the Site is the property of the Employer. The Contractor is to notify the Employer of such discoveries and carry out the Employer's instructions for dealing with them.

18. Possession of the Site

18.1 The Employer shall give possession of all parts of the Site to the Contractor. If possession of a part is not given by the date stated in the Contract Data the Employer is deemed to have delayed the start of the relevant activities and this will be Compensation Event.

19. Access to the Site


19.1 The Contractor shall allow the Employer and any person authorized by the Employer access to the Site, to any place where work in connection with the Contract is being carried out or is intended to be carried out and to any place where materials or plant are being manufactured / fabricated / assembled for the works.

20. Instructions

20.1 The Contractor shall carry out all instructions of the Employer which comply with the applicable laws where the Site is located.

B. Time Control

21. Program


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

- 21.1 Within the time stated in the Contract Data the Contractor shall submit to the Employer for approval a Program showing the general methods, arrangements, order, and timing for all the activities in the Works.
- 21.2 The Employer's approval of the Program shall not alter the Contractor's obligations. The Contractor may revise the Program and submit it to the Employer again at any time. A revised Program is to show the effect of Variations and Compensation Events.

22. Extension of the Intended Completion Date

- 22.1 The Employer shall extend the Intended Completion Date if a Compensation Event occurs or a Variation is issued which makes it impossible for Completion to be achieved by the Intended Completion Date.
- 22.2 The Employer shall decide whether and by how much to extend the Intended Completion Date within 21 days of the Contractor asking the Employer for a decision upon the effect of a Compensation Event or Variation and submitting full supporting information.

23. Delays ordered by the Employer

- 23.1 The Employer may instruct the Contractor to delay the start or progress of any activity within the Works.

24. Management meetings

- 24.1 The Employer may require the Contractor to attend a management meeting. The business of a management meeting shall be to review the progress achieved and the plans for remaining work.
- 24.2 The responsibility of the parties for actions to be taken is to be decided by the Employer either at the management meeting or after the management meeting and stated in writing to be distributed to all who attended the meeting.

C. Quality Control

25. Identifying defects

- 25.1 The Employer shall check the Contractor's work and notify the Contractor of any Defects that are found. Such checking shall not affect the Contractor's responsibilities. The Employer may instruct the Contractor to search for a Defect and to uncover and test any work that the Employer considers may have a Defect.

26. Tests

- 26.1 If the Employer instructs the Contractor to carry out a test not specified in the Specification to check whether any work has a Defect and the test shows that it does, the Contractor shall pay for the test and any samples. If there is no Defect the test shall be a Compensation Event.

27. Correction of defects

- 27.1 The Employer shall give notice to the Contractor of any Defects before the end of the Defects Liability Period, which begins at Completion and is defined in the Contract Data. The Defects Liability Period shall be extended for as long as Defects remain to be corrected.
- 27.2 Every time notice of a Defect is given, the Contractor shall correct the notified Defect within the length of time specified by the Employer's notice.

28. Uncorrected defects

- 28.1 If the Contractor has not corrected a Defect within the time specified in the Employer's notice, the Employer will assess the cost of having the Defect corrected, and the Contractor will pay this amount.

D. Cost Control

29. Bill of Quantities (BOQ)

- 29.1 The BOQ shall contain items for the construction, installation, testing, and commissioning work to be done by the Contractor.

T. J.

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

29.2 The BOQ is used to calculate the Contract Price. The Contractor is paid for the quantity of the work done at the rate in the BOQ for each item

30. Variations

30.1 The Employer shall have power to order the Contractor to do any or all of the following as considered necessary or advisable during the progress of the work by him

- (a) Increase or decrease of any item of work included in the Bill of Quantities (BOQ);
- (b) Omit any item of work;
- (c) Change the character or quality or kind of any item of work;
- (d) Change the levels, lines, positions and dimensions of any part of the work;
- (e) Execute additional items of work of any kind necessary for the completion of the works; and
- (f) Change in any specified sequence, methods or timing of construction of any part of the work.

30.2 The Contractor shall be bound to carry out the work in accordance with any instructions in this connection, which may be given to him in writing by the Employer and such alteration shall not vitiate or invalidate the contract.

30.3 Variations shall not be made by the Contractor without an order in writing by the Employer, provided that no order in writing shall be required for increase or decrease in the quantity of an item appearing in the BOQ so long as the work executed conforms to the approved drawings.

30.4 The Contractor shall promptly request in writing the Employer to confirm verbal orders and if no such confirmation is received within 15 days of request, it shall be deemed to be an order in writing by the Employer.

31. Payments for Variations

31.1 Payment for increase in the quantities of an item in the BOQ up to 25% of that provided in the Bill of Quantities shall be made at the rates quoted by the Contractor.

31.2 For quantities in excess of 125% of the tendered quantity of an item as given in the BOQ, the Contractor shall be paid at the rate entered in or derived from, in the Schedule of Rates (applicable for the area of the work and current at the time of award of contract) plus or minus the overall percentage of the original tendered rates over the current Schedule of Rates prevalent at the time of award of contract.

31.3 If there is no rate for the additional, substituted or altered item of the work in the BOQ, efforts would be made to derive the rates from those given in the BOQ or the Schedule of Rates (applicable for the area of the work and current at the time of award of contract) and if found feasible the payment would be made at the derived rate for the item plus or minus the overall percentage of the original tendered rates over the current Schedule of Rates prevalent at the time of award of contract

31.4 If the rates for additional, substituted or altered item of work cannot be determined either as at 31.1, 31.2 or 31.3 above, the Contractor shall be requested to submit his quotation for the items supported by analysis of the rate or rates claimed, within 7 days.

31.5 If the Contractor's quotation is determined unreasonable, the Employer may order the Variation and make a change to the Contract Price which shall be based on Employer's own forecast of the effects of the Variation on the Contractor's costs.

31.6 If the Employer decides that the urgency of varying the work would prevent a quotation being given and considered without delaying the work, no quotation shall be given and the Variation shall be treated as a Compensation Event.

31.7 Under no circumstances the Contractor shall suspend the work on the plea of non-settlement of rates for items falling under this Clause.

32. Submission of bills for payment

32.1 The Contractor shall submit to the Employer monthly bills of the value of the work completed less the cumulative amount paid previously.

32.2 The Employer shall check the Contractor's bill and determine the value of the work executed which shall comprise of (i) value of the quantities of the items in the BOQ completed and (ii) valuation of Variations and Compensation Events.

32.3 The Employer may exclude any item paid in a previous bill or reduce the proportion of any item previously paid in the light of later information.

33. Payments

33.1 Payments shall be adjusted for deductions for retention, other recoveries in terms of the contract and taxes, at source, as applicable under the law. The Employer shall pay the Contractor the within 60 days of submission of bill.

33.2 Items of the Works for which no rate or price has been entered in will not be paid for by the Employer and shall be deemed covered by other rates and prices in the Contract.

34. Compensation events

34.1 The following are Compensation events unless they are caused by the Contractor:

(a) The Employer does not give access to a part of the Site by the Site Possession Date stated in the Contract Data.

(b) The Employer orders a delay or does not issue drawings, specifications or instructions required for execution of works on time.

(c) The Employer instructs the Contractor to uncover or to carry out additional tests upon work which is then found to have no Defects.

(d) The Employer gives an instruction for dealing with an unforeseen condition, caused by the Employer, or additional work required for safety or other reasons.

(e) The effect on the Contractor of any of the Employer's Risks.

(f) The Employer unreasonably delays issuing a Certificate of Completion.

(g) Other Compensation Events listed in the Contract Data or mentioned in the Contract.

34.2 If a Compensation Event would cause additional cost or would prevent the work being completed before the Intended Completion Date, the Contract Price shall be increased and/or the Intended Completion Date is extended. The Employer shall decide whether and by how much the Contract Price shall be increased and whether and by how much the Intended Completion Date shall be extended.

34.3 As soon as information demonstrating the effect of each Compensation event upon the Contractor's forecast cost has been provided by the Contractor, it is to be assessed by the Employer and the Contract Price shall be adjusted accordingly. If the Contractor's forecast is deemed unreasonable, the Employer shall adjust the Contract Price based on Employer's own forecast. The Employer will assume that the Contractor will react competently and promptly to the event.

34.4 The Contractor shall not be entitled to compensation to the extent that the Employer's interests are adversely affected by the Contractor not having given early warning or not having cooperated with the Employer.

35. Tax

- 35.1 The rates quoted by the Contractor shall be deemed to be inclusive of the sales and other taxes that the Contractor will have to pay for the performance of this Contract. The Employer will perform such duties in regard to the deduction of such taxes at source as per applicable law.

36. Liquidated damages

- 36.1 The Contractor shall pay liquidated damages to the Employer at the rate per day stated in the Contract Data for each day that the Completion Date is later than the Intended Completion Date. The total amount of liquidated damages shall not exceed the amount defined in the Contract Data. The Employer may deduct liquidated damages from payments due to the Contractor. Payment of liquidated damages does not affect the Contractor's liabilities.

- 36.2 If the Intended Completion Date is extended after liquidated damages have been paid, the Employer shall correct any overpayment of liquidated damages by the Contractor by adjusting the next payment of bill.

37. Cost of repairs

- 37.1 Loss or damage to the Works or Materials to be incorporated in the Works between the Start Date and the end of the Defects Correction periods shall be remedied by the Contractor at the Contractor's cost if the loss or damage arises from the Contractor's acts or omissions.

E. Finishing the Contract

38. Completion

- 38.1 The Contractor shall request the Employer to issue a Certificate of Completion of the Works and the Employer will do so upon deciding that the Work is completed.

39. Taking over

- 39.1 The Employer shall take over the Site and the Works within seven days of issuing a certificate of Completion.

40. Final account

- 40.1 The Contractor shall supply to the Employer a detailed account of the total amount that the Contractor considers payable under the Contract before the end of the Defects Liability Period. The Employer shall issue a Defect Liability Certificate and certify any final payment that is due to the Contractor within 90 days of receiving the Contractor's account if it is correct and complete. If it is not, the Employer shall issue within 90 days a schedule that states the scope of the corrections or additions that are necessary. If the Final Account is still unsatisfactory after it has been resubmitted, the Employer shall decide on the amount payable to the Contractor and make payment within 60 days of receiving the Contractor's revised account.

41. As built drawings

- 41.1 If "as built" Drawings¹⁷ are required, the Contractor shall supply them by the dates stated in the Contract Data.
- 41.2 If the Contractor does not supply the Drawings by the dates stated in the Contract Data, or they do not receive the Employer's approval, the Employer shall withhold the amount stated in the Contract Data from payments due to the Contractor.

42. Termination

- 42.1 The Employer or the Contractor may terminate the Contract if the other party causes a fundamental breach of the Contract.
- 42.2 Fundamental breaches of Contract include, but shall not be limited to the following:
- (a) the Contractor stops work for 45 days when no stoppage of work is shown on the current Program and the stoppage has not been authorized by the Employer;

- (b) the Employer instructs the Contractor to delay the progress of the Works and the instruction is not withdrawn within 60 days;
- (c) The Contractor becomes bankrupt or goes into liquidation other than for a reconstruction or amalgamation;
- (d) a payment due to the Contractor is not paid by the Employer within 90 days of the date of the submission of the Bill by Contractor;
- (e) the Employer gives Notice that failure to correct a particular Defect is a fundamental breach of Contract and the Contractor fails to correct it within a reasonable period of time determined by the Employer;
- (f) the Contractor does not maintain a security which is required;

¹⁷ Completion drawings

- (g) the Contractor has delayed the completion of works by the number of days for which the maximum amount of liquidated damages can be paid as defined in the Contract data; and
- (h) if the Contractor, in the judgment of the Employer has engaged in corrupt or fraudulent practices in competing for or in the executing the Contract.

For the purpose of this paragraph : "corrupt practice" means the offering, giving, receiving or soliciting of any thing of value to influence the action of a public official in the procurement process or in contract execution. "Fraudulent practice" means a misrepresentation of facts in order to influence a procurement process or the execution of a contract to the detriment of the Borrower, and includes collusive practice among Tenderers (prior to or after Tender submission) designed to establish Tender prices at artificial non-competitive levels and to deprive the Borrower of the benefits of free and open competition."

42.3 When either party to the Contract gives notice of a breach of contract to the Employer for a cause other than those listed under Sub Clause 42.2 above, the Employer shall decide whether the breach is fundamental or not.

42.4 Notwithstanding the above, the Employer may terminate the Contract for convenience.

42.5 If the Contract is terminated the Contractor shall stop work immediately, make the Site safe and secure and leave the Site as soon as reasonably possible.

43. Payment upon Termination

43.1 If the Contract is terminated because of a fundamental breach of Contract by the Contractor, the Employer shall prepare bill for the value of the work done less advance payments received up to the date of the bill, less other recoveries due in terms of the contract, less taxes due to be deducted at source as per applicable law and less the percentage to apply to the work not completed as indicated in the Contract Data. Additional Liquidated Damages shall not apply. If the total amount due to the Employer exceeds any payment due to the Contractor the difference shall be a debt payable to the Employer.

43.2 If the Contract is terminated at the Employer's convenience or because of a fundamental breach of Contract by the Employer, the Employer shall prepare bill for the value of the work done, the reasonable cost of removal of Equipment, repatriation of the Contractor's personnel employed solely on the Works, and the Contractor's costs of protecting and securing the Works and less advance payments received up to the date of the certificate, less other recoveries due in terms of the contract, and less taxes due to be deducted at source as per applicable law and make payment accordingly.

44. Property

44.1 All materials on the Site, Plant, Equipment, Temporary Works and Works are deemed to be the property of the Employer, if the Contract is terminated because of a Contractor's default.

45. Release from performance

45.1 If the Contract is frustrated by any event entirely outside the control of either the Employer or the Contractor the Employer shall certify that the Contract has been frustrated. The Contractor shall make the Site safe and stop work as quickly as possible after receiving this certificate and shall be paid for all work carried out before receiving it and for any work carried out afterwards to which commitment was made.

F. Special Conditions of Contract

1. Labour :

The Contractor shall, unless otherwise provided in the Contract, make his own arrangements for the engagement of all staff and labour, local or other, and for their payment, housing, feeding and transport. The Contractor shall, if required by the Employer, deliver to the Employer a return in detail, in such form and at such intervals as the Employer may prescribe, showing the staff and the numbers of the several classes of labour from time to time employed by the Contractor on the Site and such other information as the Employer may require.

2. Compliance with labour regulations :


During continuance of the contract, the Contractor and his sub contractors shall abide at all times by all existing labour enactments and rules made there under, regulations, notifications and bye laws of the State or Central Government or local authority and any other labour law (including rules), regulations, bye laws that may be passed or notification that may be issued under any labour law in future either by the State or the Central Government or the local authority. The Contractor shall keep the Employer indemnified in case any action is taken against the Employer by the competent authority on account of contravention of any of the provisions of any Act or rules made there under, regulations or notifications including amendments. If the Employer is caused to pay or reimburse, such amounts as may be necessary to cause or observe, or for non-observance of the provisions stipulated in the notifications/bye laws/Acts/Rules/regulations including amendments, if any, on the part of the Contractor, Employer shall have the right to deduct any money due to the Contractor including his amount of security deposit. The Employer shall also have right to recover from the Contractor any sum required or estimated to be required for making good the loss or damage suffered by the Employer.

The employees of the Contractor and the Sub-Contractor in no case shall be treated as the employees of the Employer at any point of time.

3. Protection of Environment:

The contractor shall take all reasonable steps to protect the environment on and off the Site and to avoid damage or nuisance to persons or to property of the public or others resulting from pollution, noise or other causes arising as a consequence of his methods of operation. During continuance of the contract, the contractor and his sub-contractors shall abide at all times by all existing enactments on environmental protection and rules made there under, regulations, notifications and bye-laws of the State or Central Government, or local authorities and any other law, bye-law, regulations that may be passed or notification that may be issued in this respect in future by the State or Central Government or the local authority.

[Add other Clauses specific to the work for which tenders are invited.]


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore

SECTION 5: CONTRACT DATA

Items marked "N/A" do not apply in this Contract.

The following documents are also part of the Contract: **Clause Reference**

The Employer is :

Name: The Commissioner

Address: Bruhat Bangalore Mahanagara Palike

N.R.Square, Bangalore - 560072

Name of authorized Representative: Executive Engineer

The name and identification number of the Contract is

[insert name and number as indicated in the Invitation for Tenders]. [1.1]

The Works consist of -----

[brief summary, including relationship to other contracts under the Project].

The start date shall be the date of issue of notice to proceed with the work. [1.1]

The Intended Completion Date for the whole

of the Works is -----¹⁸ [15, 22]

The following documents also form part of the Contract: [2.2]

The Site Possession Date is: ¹⁹ [18]

The Site is located at _____ [1.1]

and is defined in drawings nos. _____


The Defects Liability Period is 11 months.

The liquidated damages for the whole of the works are

Rs. _____ (amount) per day ²¹ [36]

¹⁸ At the time of preparation of the tender document give the period required for completion of work. When the Agreement is drawn after award of the contract, the dates can be put in.

¹⁹ At the time of preparation of the tender document give the period after the issue of work order, when the site would be made available to the contractor for example 'one week after the issue of work order'.


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

²⁰ The period should depend upon the period required for testing of the work. In case of building it could be 12 months (passing of one rainy season); for pipe laying work, tanks, water retaining structures, the time required for testing; for canals, lining works, the passing of one monsoon or running of canal which ever is lower; roads and highways passing of one monsoon (12 months)

²¹ The amount is usually computed on the basis of 0.1% the contract price per day. The amount has to be specified as a round figure nearest to the hundred.

The maximum amount of liquidated damages for the whole of the works [36]
is ten percent of final contract price.

The date by which "as-built" ²² drawings (in scale ...) in 2 sets are required is within 30 days of issue of certificate of completion .. [41]

The amount to be withheld for failing to supply "as built" ²³ drawings by the date required is
Rs. _____ [41]

The following events shall also be fundamental breach of the contract : [42.2]


1. The contractor has contravened Sub-clause 7.1 and Clause 9 of CC.

The percentage to apply to the value of the work not completed representing the Employer's [43.1]
additional cost for completing the Works shall be 30²⁴ percent.

²² Completion drawings

²³ The amount should be sufficient to get the completion drawings prepared by alternative agency in case the contractor fails to submit.

²⁴ Change if need be. It should be sufficient to get the balance works completed by alternative agency.


Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

[illegible]

Note:

- (1) Item for which no rate or price has been entered in will not be paid for by the Employer when executed and shall be deemed covered by the other rates and prices in the Bill of Quantities (refer: ITB Clause 7.2 and CC Clause 33.2).
- (2) Unit rates and prices shall be quoted by the Tenderer in Indian Rupees.
- (3) Where there is a discrepancy between the rate in figures and words, the rates in words will govern.
[ITB Clause 19.1(a)]
- (4) Where there is a discrepancy between the unit rate and the line item total resulting from multiplying the unit rate by quantity, the unit rate quoted shall govern [ITB Clause 19.1 (b)]

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92
